



Adare Rathkeale Municipal District

District Engineer's Report



Adare Rathkeale Municipal District Meeting

July 9th 2019

Delivered by: Aidan Finn SEE

TABLE OF CONTENTS

	Page
1 Councillor Requested Reports	3
1.1 Drainage Issues at Courtmatrix	
1.2 Flooding Issues in Foynes	
1.3 Marine Cove, Foynes	
1.4 Slí na Sláinte, Askeaton	
2 Update on Schedule of MD Works Progress	4
3 Progress on other funded works	7
3.1 Development Funds	
3.2 Foynes Minor Flood Relief Scheme	
3.3 Foynes Yacht Club Rock Armouring	
3.4 Slí na Sláinte, Askeaton	
3.5 Local Improvement Schemes	
4 Applications for funding made	9
4.1 Askeaton TVR Town Centre	
4.2 Askeaton ORIS 2019 Riverside Walk	
4.3 Foynes ORIS 2019 Monument Hill	
4.4. Ballingarry TVR 2019	
4.5 Gerald Griffin GAA Clar Application	
5 Update on Design Works	11
5.1 Shanagolden Traffic Calming	
5.2 Proposed Workshop on Village Improvements	

1. Councillor Requested Reports

1.1 Drainage Issues at Courtmatrix

These works will be commenced when the resources come free from working on the Roadworks Programme.

1.2 Flooding Issues at Foynes

The Municipal District has met with a telemetry contractor on site and they are shortly to commence a radio survey of the area, with a view to fitting a pressure switch at the reservoir which will connect with an actuator valve on the fire control pipe, thus regulating the reservoir depth.

Concurrently, the Municipal District has appointed a consultant to carry out Rainfall and Runoff calculations to determine the preferred depth to be maintained in the reservoir and to determine capacity requirements on the outfall culvert.

1.3 Flooding issues in Askeaton

This project is included in the works requirement for the CFRAMS project under the control of the OPW. It has not been approved under the first tranche of funding for same.

As this project is not under the control of the Municipal District, it is recommended that it be removed from the District Engineer's Report.

1.4 Marine Cove, Foynes

The Municipal District will undertake a CCTV survey of the Storm Water system in the coming weeks to determine necessary works.

1.5 Slí na Sláinte, Askeaton

Approval has been received from the TII for the proposed works. These will commence in the coming weeks.

2.0 Update on Schedule of MD Works

Road Works Scheme 2019			
Regional Roads Surface Dressing Allocation = €134,030			
Road No.	Description	Length (m)	Status
R518	Kyletaun jn to Comnys	1200	Due 2/8/19
R521	Jobbers Cross to Cosgraves Cross	1800	Complete
R516	Crean Bruff	1000	Due 2/8/19
Regional Roads Road Reconstruction Allocation = €333,200			
Road No.	Description	Length (m)	Status
R516	Crean Bruff	400	Macadam in progress, S/D due 2/8
R518	Askeaton Main Street Overlay	600	Complete
R523	Reens towards Skehanagh	200	Due 30/8/19
Local Roads Surface Dressing Allocation = €357,004			
Road No.	Description	Length (m)	Status
L6119	Shanid Lower Road	1772	Complete
L1242	Ardnaveagh Rathkeale	1000	Due 2/8/19
L6014	Kennedys X towards Kilcornan	700	Complete
L6057	Golf Club Rd	1500	Due 2/8/19
L8023	Kiltenan Road from L1206 Jn towards Croagh	450	Due 2/8/19
L6028	From L1206 Jn towards Ballinguile	750	Due 2/8/19
L1203	Rathkeale to Cappagh Rd from Rousemountr Jn to Roches Rd Jn	1300	Due 2/8/19
L1208	Ballingarry to Croom Road from Cahills R519 Jn to kilmacow X Part 1	1900	Due 30/8/19
L1219	Kilbradran Graveyard Towards Lissatotan	800	Complete
L8606	Morenane	950	Due 30/8/19
L8016	Mainster South	1900	Due 30/8/19
L1409	Grange More Crecora	1600	Due 30/8/19

Local Roads			
Road Reconstruction Allocation = €1,302,820			
Road No.	Description	Length (m)	Status
L6110	Kilterry Cross to Stacks Cross	900	Complete
L6098	Coolle Road Killaney	1,550	Complete
L12016	Laundry Road Castletown	1,100	Complete
L8033	Kennedys X Monanooag to Cloraine	1,000	Complete
L1241	Glenameade to Tobermurray Rd	200	Due 30/8/19
L6010	Shanongrove to Shanpallas Road	250	Deferred to 2020
L6025	Amagon More Link Road	1,000	In progress, S/D 2/8/19
L1206	Nevilles to Kiltenan	1,300	In progress, S/D 2/8/19
L14201	Caherass Road	600	Due 30/8/19
L1250	Askeaton Slip road to N69	140	Complete
L6182	Thomas Street Rathkeale	300	Due 9/7/19
L1419	Carrigeen	800	Ralumac complete, S/D 2/8/19
L1410	Mainister	700	In Progress, S/D 2/8/19
L8656	Kilmore	500	Due 30/8/19
L8016	Ballymacsradeen East	200	Due 30/8/19
L1418	Carrow	400	Deferred to 2020
L1407	Greenmount to Crecora	800	Due 30/8/19
Bridge Rehabilitation Work Structures (STR) Allocation = € 185,000			
Road No.	Description	Length (m)	Status
L6150	Ballingarry	N/A	Design only this year
R521	Shanagolden Culvert	N/A	
L1222	Ballylin	N/A	
R516	Tullovin Bridge	N/A	Design Only this year
	Total		€185,000
Low Cost Safety Improvement Schemes (LCSI) Allocation = € 44,000			
Road No.	Description	Length (m)	Status
R518	Rylands, Ballingarry	N/A	Pedestrian Crossings and Driver Feedback Signs ordered
Drainage Works Allocation = €200,000			
Road No.	Description	Length (m)	Status
R518	Courtmatrix	450	Due 30/9/19
R512	Shreelane Shanagolden	450	Due 30/10/19

R518	Rathkeale Underpass at Holycross	300	Due 19/7/19
L6110	Kilteery	120	Due 30/9/19
Specific Improvement Grant Allocation = €500,000			
Road No.	Description	Length (m)	Status
	Croom Distributor Road	N/A	Ready to appoint contractor, works expected to commence next month


3 Progress on other funded Works

3.1 Development Funded Works

Area	Description (Development Fund 2019)	Progress
AR	New walkway outside St. Nicholas School, Adare	Currently being designed
AR	Ballingarry Footpaths and Pedestrian Crossing	Footpath completed outside Mustard Seed, pedestrian crossing at the school awaiting completion of building works there
AR	Junction Improvements Pallaskenry	Preliminary Design Complete
AR	Pedestrian Crossing Rathkeale Library	Designed



Rathkeale Library Pedestrian Crossing

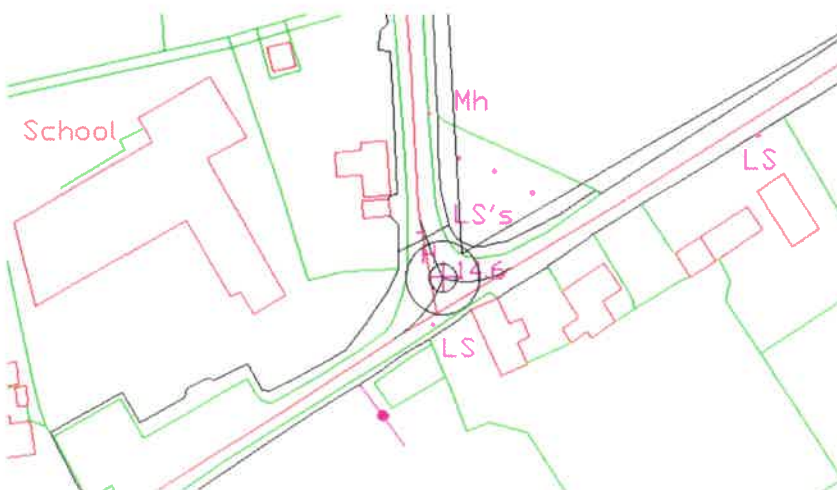

Preliminary Design of Proposed Mini Roundabout Pallaskenry

3.2 Foynes Minor Flood Relief Scheme


The Municipal District proposes to utilise telemetry to regulate the depth of water in the reservoir, thus utilising the reservoir for attenuation for storm events. To this end: Telemetry Contractor appointed, Rainfall runoff calculations consultant appointed. Survey Contractor to be appointed shortly

3.3. Foynes Yacht Club Rock Armouring


OPW funding of €128,025 received. Initial meeting regarding scope of works held on site 27/6/19.

3.4 Slí na Sláinte, Askeaton

TII Approval of Works received. Scope of works now extended to bridge over the River Deel. Estimated cost of work now €227,000, with €118,000 received from ORIS 2018 and balance to come from the TII. Works to commence shortly.

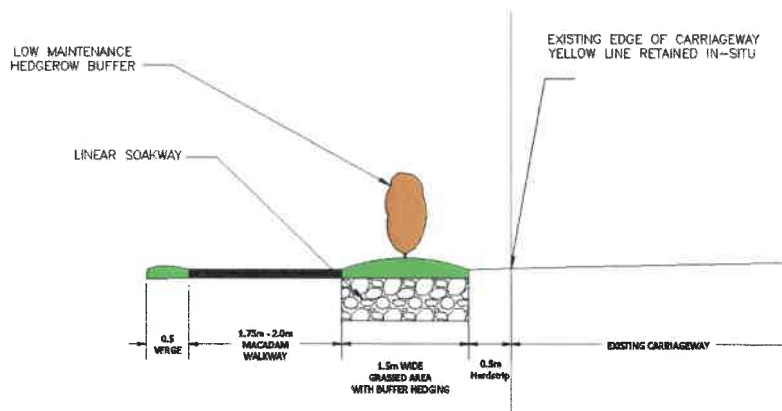

Askeaton Slí na Sláinte Detail

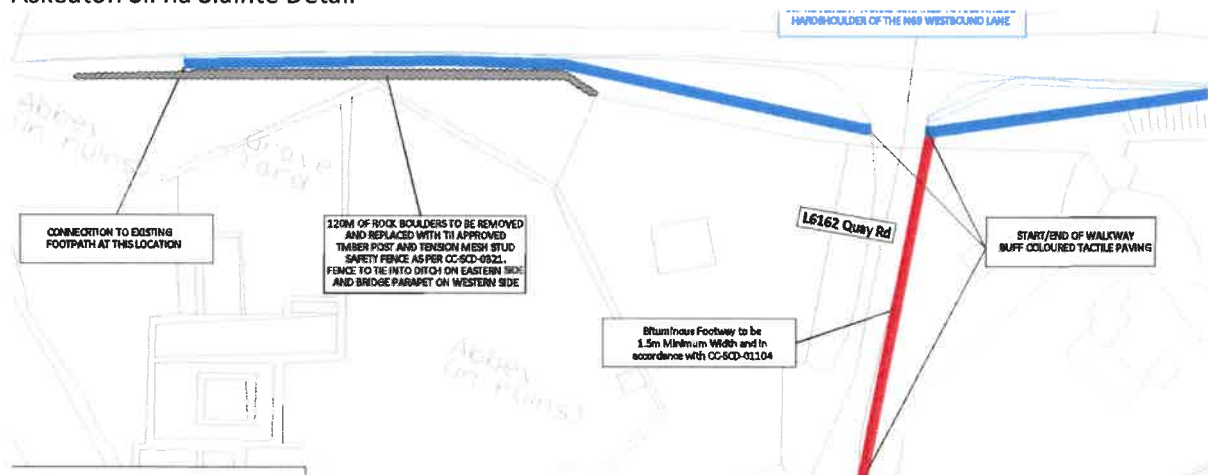

Askeaton Slí na Sláinte Extension

3.5 Local Improvement Schemes

Ballyshonik, Pallaskenry – Complete
Ringmoylan, Pallaskenry – Due 8/7/19
Drehidtrasna, Adare – Due 2/8/19

4 Report on Applications for funding made

4.1 Askeaton TVR Town Centre

Application has been made for €200,000 from TVR to go with €200,000 council funds to progress Town Centre Improvements in Askeaton. The Part 8 Planning process for these works will commence shortly.



4.2 Askeaton ORIS 2019 Riverside Walk

Application has been made for €96,000 to extend the Riverside Walk in Askeaton.




4.3 Foynes ORIS 2019 Monument Hill

Application has been made for €168,000 to reinstate the public walkway to the Monument in Foynes.



4.4. Ballingarry TVR 2019

Ballingarry Development Association has made an application for €99,500 to re develop the Mall, Ballingarry.

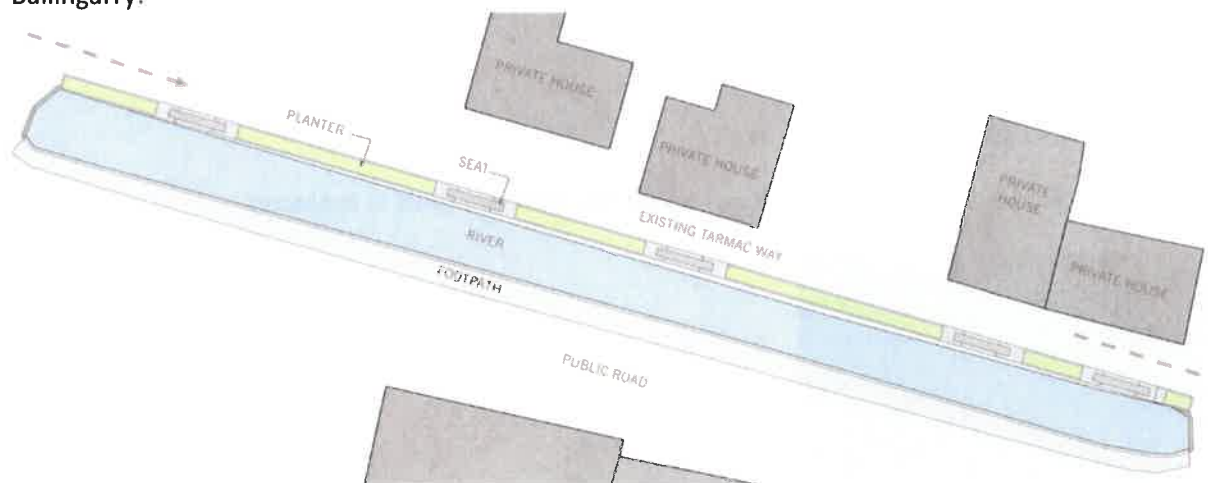

Proposed Works, The Mall, Ballingarry


4.5 Gerald Griffin GAA Clar Application

Gerald Griffin GAA club in Ballyhahill has made application for €30,000 to resurface its carpark.

5 Update on Design Works

5.1 Shanagolden Traffic Calming

A traffic calming layout has been designed for Shanagolden. Funding will be applied for in 2020 under the Low Cost Safety Improvement Scheme.

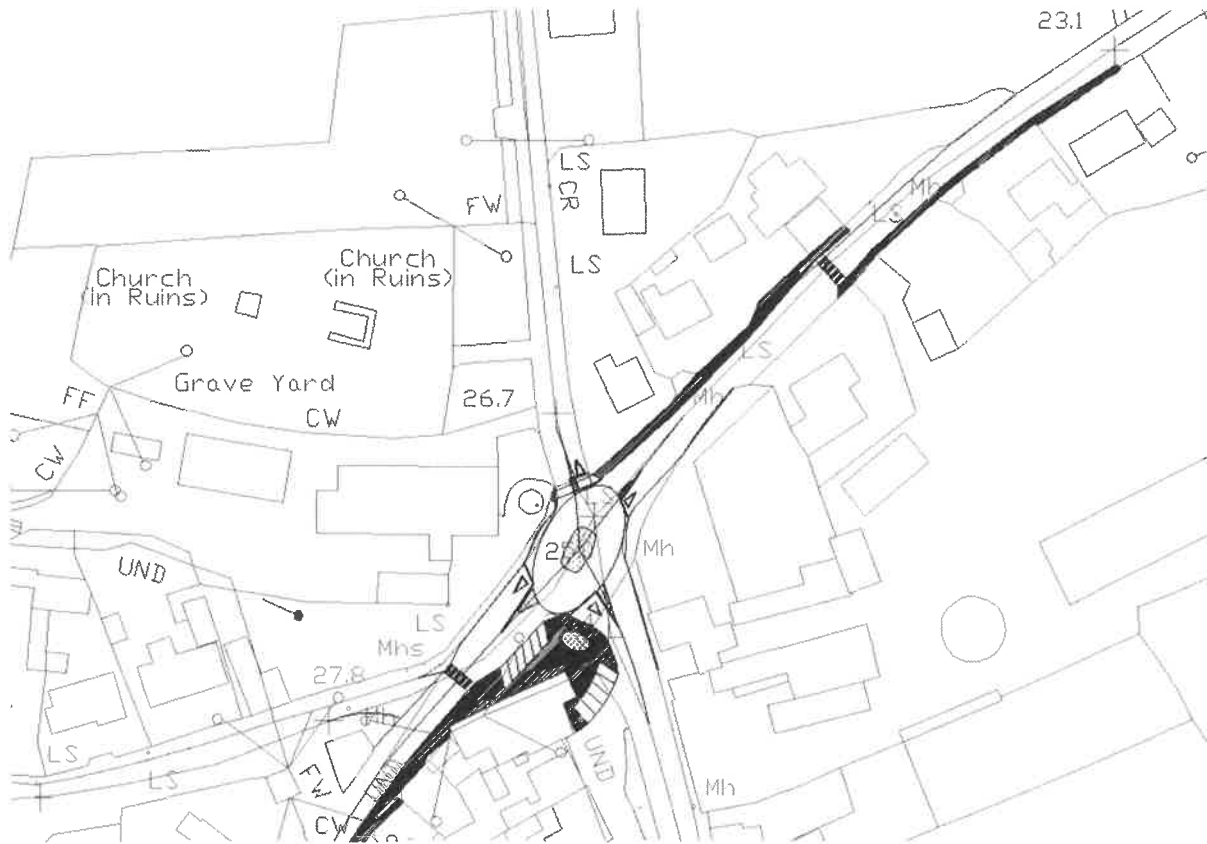

Shanagolden Traffic Calming

5.2 Proposed Workshop on Village Improvements

Numerous ideas have been expressed in relation to works requirements in the various villages in the Municipal District. It would be helpful to discuss with the members the following:

1. What are the priorities for delivery in each of the villages.
2. Funding options for delivery of these priorities.

The aim would be to document the requirements and seek to deliver on them within the timeframe of the Council.
