



Comhairle Cathrach  
& Contae **Luimnigh**

**Limerick City**  
& County Council

**Adare Rathkeale Municipal District  
District Engineer's Report**



**Adare Rathkeale Municipal District Meeting  
June 9th 2020**

**Delivered by: Aidan Finn SEE**

## TABLE OF CONTENTS

	<b>Page</b>
1 Councillor Requested Reports	3
2 Schedule of MD Works	3
3 Progress on other funded works	6
3.1 Development Funds	
3.2 Foynes Minor Flood Relief Scheme	
3.3 Foynes Yacht Club	
3.3 Low Cost Safety Schemes	
3.4 Askeaton TVR Town Centre	
3.5 Ballingarry TVR The Mall	
4 General Updates for the District	12
4.1 Adare Rathkeale 5 Year Plan	
4.2 Update from Central Services	
4.3 Parking	
4.4 TII Funded Works	
4.5 Glenameade Oil Spill	
4.6 Design and Delivery Update	

## 1. Councillor Requested Reports

There are currently no outstanding Councillor Requested Reports.

## 2. Update on Schedule of MD Works

<b>ADARE RATHKEALE MUNICIPAL DISTRICT Road Works Schemes 2020</b>				
<b>Regional Roads Road Reconstruction Allocation € 786,601</b>				
<b>Road No.</b>	<b>Description</b>	<b>Length (m)</b>	<b>Total Cost €</b>	<b>Status</b>
R518	Rathkeale - Danahers Cross to Cois Deel	525	€254,000	In Progress. Drainage works underway.
R518	Ballingarry - Rylands to Grotto	500	€400,334	
R521	Shanagolden Main Street Jn	200	€50,000	
R516	Croom Main Street Jn	100	€20,000	
R521	Shroolane Trench Reinstatement	450	€32,262	Works Complete
R521	Corbally Bends	130	€30,005	Works Complete
<b>Total</b>		<b>1,905</b>	<b>€786,601</b>	

<b>Regional Roads Surface Dressing Allocation € 136,785</b>				
<b>Road No.</b>	<b>Description</b>	<b>Length (m)</b>	<b>Total Cost €</b>	<b>Status</b>
R521	Cosgraves Cross towards Kate Dalys-Section 1	1,200	€46,200	Works Complete
R523	Reens to Ardagh	1,930	€63,690	Works Complete
R512	Ballyneety to Manister Rd	815	€26,895	Preparatory Works Completed
<b>Total</b>		<b>3,945</b>	<b>€136,785</b>	

<b>Local Roads Surface Dressing Allocation € 505,583</b>				
<b>Road No.</b>	<b>Description</b>	<b>Length (m)</b>	<b>Total Cost €</b>	<b>Status</b>
L1422	Samco Jn to Kilgrogan Jn	1,200	€29,700	Works Complete
L1423	Shauntraud Jn Carnane	800	€19,800	Works Completed
L1201	Askeaton to Moig RM	1200	€29,700	Works Completed
L6066	Bartholemews	2100	€47,250	Works Completed
L1221	Ballycullen to Askeaton	1200	€27,000	Works Complete
L1423	Capparoe to Monanooag RM	1395	€34,526	80% Complete

L1203	Callow Jn towards Cheps Cross	1300	€32,175	Works Complete
L1208	Lynchs Shop to Dollas	1,500	€40,500	
L1408	Crecora Jn to Bawnacouma Jn	1,300	€32,175	
L1408	Crecora to Shanacloough Jn	980	€21,402	
L1208	Ballingarry to Croom Road from R519 Jn to kilmacow X Part 2	2,077	€51,405	
L1420	Caherass Jn Towards Adare	1,450	€39,150	
L8004	Manister School to Mortgage	2,000	€31,500	Preparatory Works Completed
L1416	N21 Banogue Jn towards Maigne Bridge	1,100	€27,225	
L8003	Manister School to Kilcurly	1700	€42,075	
	<b>Total</b>	<b>21,302</b>	<b>€505,583</b>	
<b>Local Roads Road Reconstruction Allocation € 1,042,376</b>				
Road No.	Description	Length (m)	Total Cost €	Status
L12143	Rylands Estate	200	€42,759	
L1227	Ballyhahill to Gaa Field Jn	1550	€125,550	80% Complete
L1227	Shanagolden to Cloonaclohessy Depot	1200	€108,000	80% Complete
L1423	Capparoo to Monanooag RI	760	€75,240	Works Complete
L8065	Shangrove	1166	€94,446	Works Complete
L8016	Ballymacscreedeen East	300	€41,177	80% Complete
L1418	Croom Concrete Road	1300	€117,000	80% Complete
L1421	Lisaleen Road From Lantern Lodge	1242	€130,638	80% Complete
L8606	Morenane to Liskennett	1200	€133,920	80% Complete
L6110	Fleanmore Cross to Four Cross Roads	874	€86,526.00	Works Complete
L1201	Askeaton to Moig RI	880	€87,120.00	Works Complete
	<b>Total</b>	<b>10,672</b>	<b>€1,042,376</b>	

<b>Low Cost Safety Improvement Schemes (LCSI) Allocation €112,000</b>				
Road No.	Description	Length (m)	Total Cost €	Status
R521	Shanagolden main Street Jn		50,000	
R511	Kellihers Cross on the R511		12,000	
R516 / L1478	Croom Junction Improvements		50,000	
	<b>Total</b>		<b>€112,000</b>	

<b>Drainage Works</b>	
-----------------------	--


<b>Allocation € 200,000</b>				
<b>Road No.</b>	<b>Description</b>	<b>Length (m)</b>	<b>Total Cost €</b>	<b>Status</b>
R521	Corbally		60,000	Works completed
L6106	Loughill Middle Road		20,000	
R523	Castlematrix		50,000	
L6114	Knockpatrick		20,000	
R518	Danaghers Cross		50,000	Commenced
<b>Total</b>			<b>€200,000</b>	

<b>Bridge Rehabilitation Allocation € 245,000</b>				
<b>Road No.</b>	<b>Description</b>	<b>Length (m)</b>	<b>Total Cost €</b>	<b>Status</b>
L6150	Ballingarry Bridge, Ballingarry		85,000	
L6119	Shanid Upper		50,000	
L1406	Doneen Bridge Crecora		25,000	
L12341	Glenbane West Cul De Sac		50,000	
L60891	Mohernagh		10,000	
L1239	Lisgordan Kilcolman		25,000	
<b>Total</b>			<b>€245,000</b>	


### 3 Progress on other funded Works

#### 3.1 Development Funded Works

Area	Description (Development Fund 2019)	Progress
AR	New walkway Dunraven Arms Hotel to the River	Works are ongoing in this area
AR	Ballingarry Footpaths and Pedestrian Crossing	Footpath completed outside Mustard Seed, river wall stabilisation works complete at the Mall. Works now proceeding at Rylanes.
AR	Junction Improvements Pallaskerry	Completed
AR	Pedestrian Crossing Rathkeale Library	Works 75% complete, awaiting contractor to complete imprinted concrete.

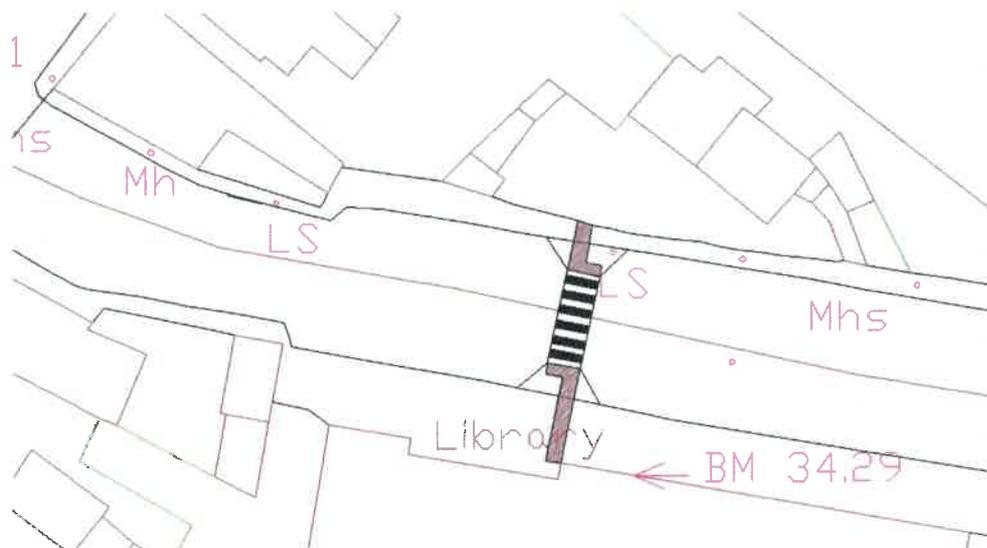

Rathkeale Library Pedestrian Crossing (revised location)

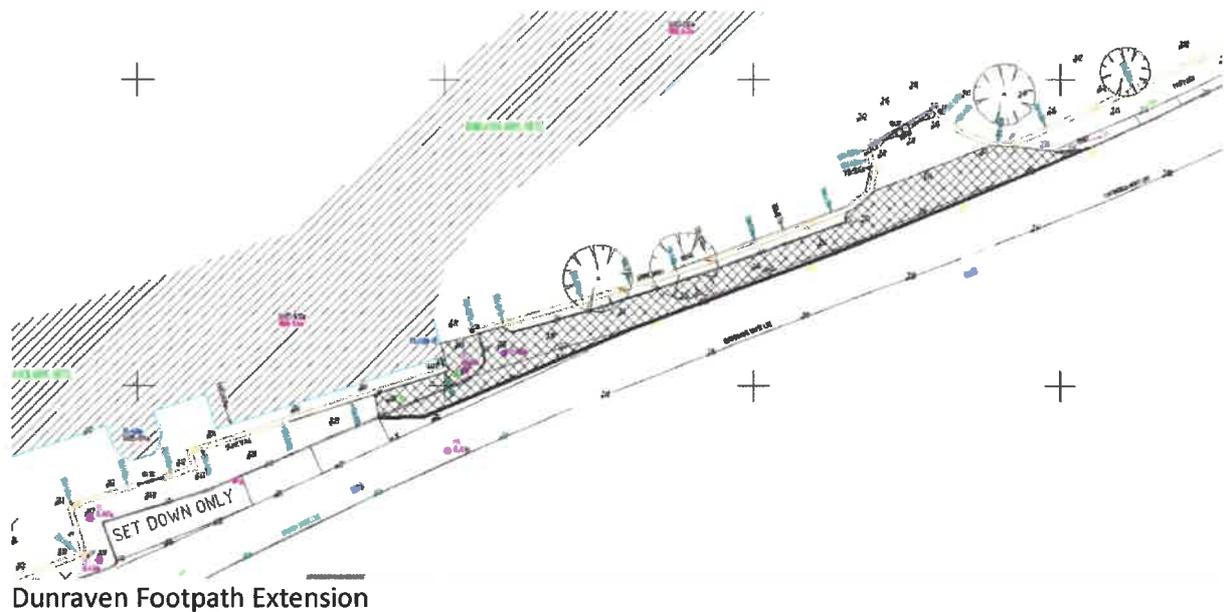

Proposed 2020 Development Contribution works (These funds will be used as seed funding against Government Grants should grants become available)

Carpark Croom €20,000

Footpath Slí na Sláinte Rathkeale €20,000

Footpath Shanagolden €20,000

### 3.2 Foynes Minor Flood Relief Scheme


The Consultant is in the advanced stages of design of the culvert, it is expected to be constructed in the Summer Months.

### 3.3 Foynes Yacht Club

Documentation has been written in a call for quotes for a Design and Build Solution to issues at this location. This will be issued to suitable Contractors this month with works expected over the summer.

### 3.3. Low Cost Safety Schemes


Funding has been received for Low Cost Safety Schemes in Shanagolden and Croom, as per the preliminary design layouts indicated below. The proposed changes to the Double yellow line extent in Croom have now been finalised and will be implemented shortly. Detailed topographical surveys of kerb lines and proposed off street parking areas in Croom will now progress to enable final design. Detailed survey of the proposed design in Shanagolden will now also progress shortly.

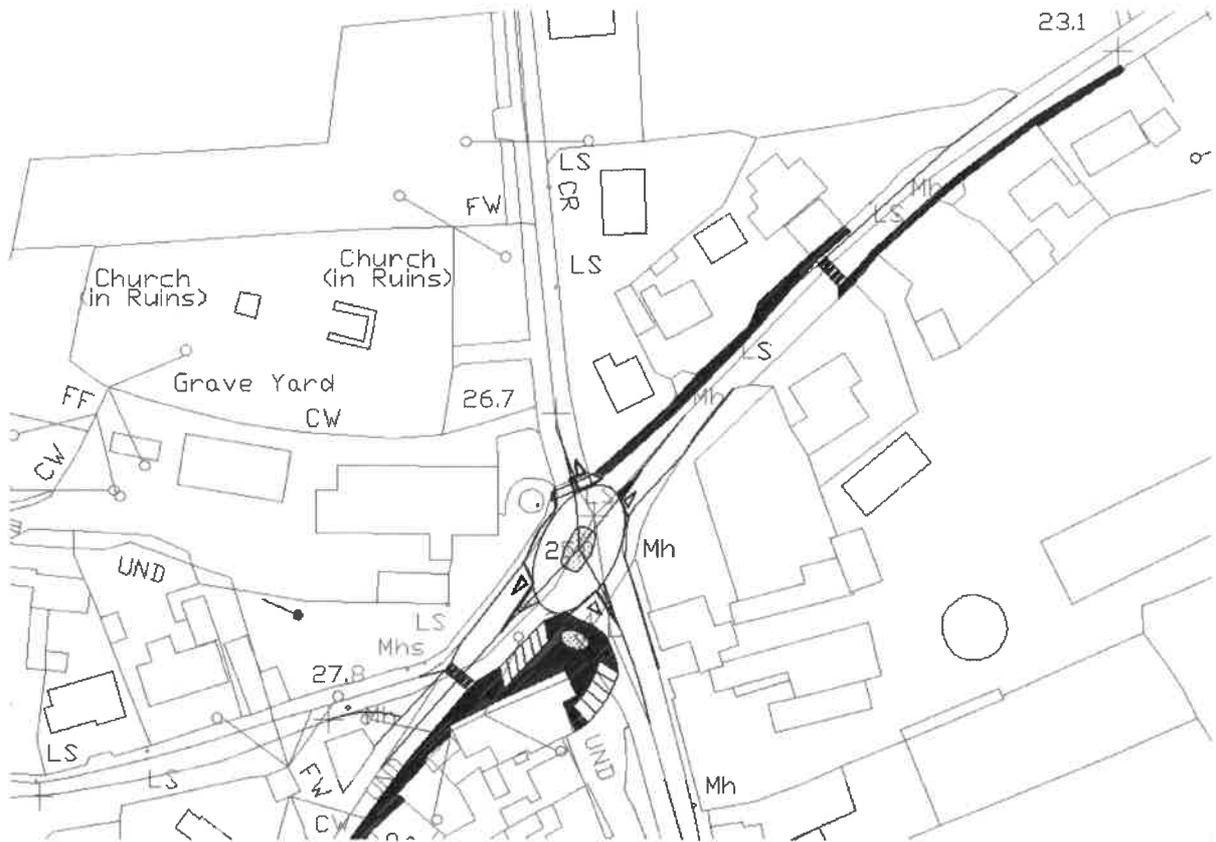

Shanagolden



Croom Parking and Junction Priority Change

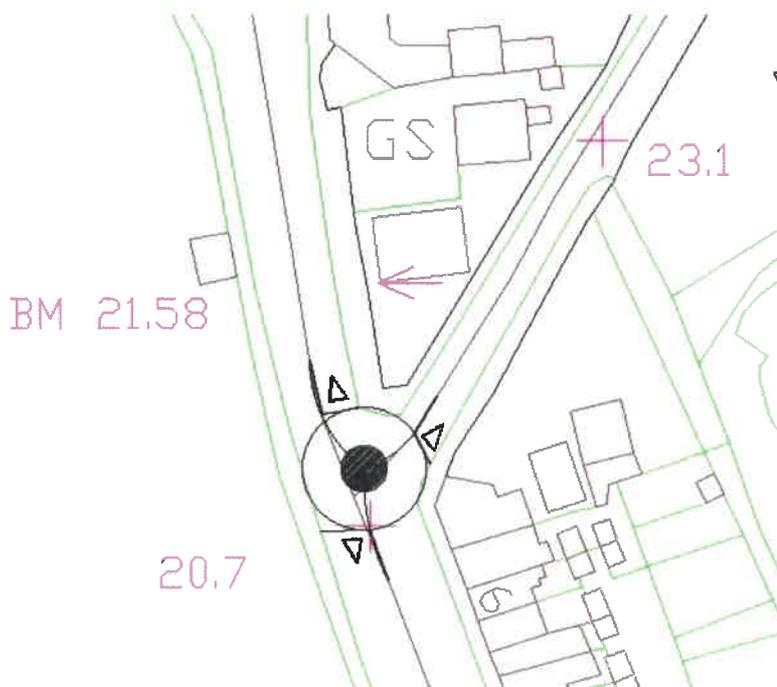

Proposed Mini Roundabout at Croom Garda Station

### 3.4 Askeaton TVR Town Centre

Limerick City and County Council has been successful in receiving a grant of €200,000 towards these works. A meeting was held on the 26<sup>th</sup> of February to discuss these works. The District Engineer is currently discussing costs of undergrounding services to determine the scope of works possible with this funding, to this end designs and costings are now being prepared by Eir and the ESB. Consultation has also now commenced on a possible one way system over the bridge.




Proposed One Way System over Castle Bridge

### 3.5 Ballingarry TVR 2019

Ballingarry Development Association has made an application to re develop the Mall, Ballingarry. LCCC has completed wall structural stability works in this channel. €79,604 has been secured in funding from the Town and Village Renewal Scheme towards this project. Final design will be subject

to a flood study currently being undertaken by Central Services.

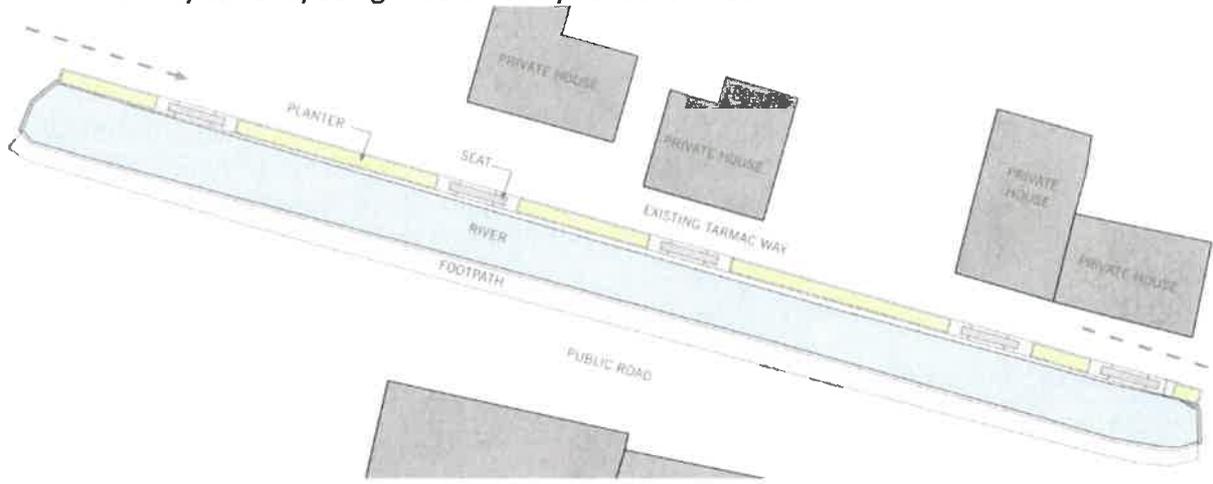

**Proposed Works, The Mall, Ballingarry**



**Ballingarry Junction Modification**

## **4 General Updates for the District**

### **4.1 Adare Rathkeale 5 Year Plan**

The first draft of the Adare Rathkeale 5 Year Plan has been completed. Delivery of this program will require the identification of funding streams. When funding streams have been identified the District Engineer will draw up a program of works. A workshop to discuss this was organised for March but was postponed due to Covid 19 restrictions, this will be reorganised when allowed.

### **4.2 Update from Central Services**

The Kilcornan Traffic Calming works are ongoing, Grass cutting on National Roads has recently been undertaken.

### **4.3 Parking**

A proposal on the Lower Main Street, Main Street, Upper Main Street area in Rathkeale is currently being drawn up.

Proposed changes to road markings in Croom to facilitate the Traffic calming works have been discussed with the Gardaí in Croom. These proposed changes will now be implemented over the coming weeks.

### **4.4 TII Funded Works**

The TII have approved funding for a footway from the Dunraven to the River Maigue in Adare. These works are well underway.

The consultants report into slope stability at Monument Hill in Foynes is being reviewed. Risks were identified and it is recommended that a further survey of the cliff face is carried out.

The TII have agreed to fund the rectification of a slope slippage at the eastern entrance to the Yacht Club area in Foynes. The proposed works are awaiting the approval of the Senior Structures Engineer.

### **4.5 Glenameade Oil Spill**

At approximately 4pm on the 16<sup>th</sup> of March a HGV carrying 28,000 litres of burnt fuel oil jack knifed on the N69 in the vicinity of Glenameade (Hegarty's Cross). The N69 was closed between Askeaton and Kildimo from the 16<sup>th</sup> to the 23<sup>rd</sup> of March, to facilitate efforts by LCCC and their Environmental Specialist Contractors Enva to clean up this oil spill, these efforts then continued under a stop go convoy system until the 3<sup>rd</sup> of April. A Temporary Speed Limit of 60km/h remains at this location until the section of road can be inspected by the TII Inspector.

### **4.6 Update from Design and Delivery**

Works recommenced on the Croom Distributor road on May 18<sup>th</sup> after lockdown.
